

Task Name	Duration	Start	Finish	Predecessors	
1 > კონტრაქტის ხელმოწერა	1 day	Mon 5/28/18 8:00	Mon 5/28/18 17:00		
2 წინასწარი ანგარიშშორება	0 days	Mon 5/28/18 17:00	Mon 5/28/18 17:00	1	
3 ელექტრობა	63 days	Tue 5/29/18 8:00	Thu 8/23/18 17:00	2	
4 კაბელები	30 days	Tue 5/29/18 8:00	Mon 7/9/18 17:00		
5 სანათების მონტაჟი	15 days	Fri 8/3/18 8:00	Thu 8/23/18 17:00		
6 მთავარი ელ. გამანაწილებელი ფარი MDB-1	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
7 მთავარი ელ. გამანაწილებელი ფარი MDB-2	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
8 მთავარი ელ. გამანაწილებელი ფარი MDB-3	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
9 მთავარი ელ. გამანაწილებელი ფარი MDB-4	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
10 მთავარი ელ. გამანაწილებელი ფარი MDB-5	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
11 ელ. გამანაწილებელი ფარი 1ს.DB-1	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
12 ელ. გამანაწილებელი ფარი 1ს.DB-2	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
13 ელ. გამანაწილებელი ფარი 1ს.DB-4	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
14 ელ. გამანაწილებელი ფარი 2ს.DB-1	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
15 ელ. გამანაწილებელი ფარი 2ს.DB-2	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
16 ელ. გამანაწილებელი ფარი 1DB-1	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
17 ელ. გამანაწილებელი ფარი 1DB-2	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
18 ელ. გამანაწილებელი ფარი 1DB-3	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
19 ელ. გამანაწილებელი ფარი 2DB-1	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
20 ელ. გამანაწილებელი ფარი 2DB-2	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
21 ელ. გამანაწილებელი ფარი 2DB-3	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
22 ელ. გამანაწილებელი ფარი 2DB-4	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
23 ელ. გამანაწილებელი ფარი 2DB-5	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
24 ელ. გამანაწილებელი ფარი 2DB-6	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
25 ელ. გამანაწილებელი ფარი 3DB-1	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
26 ელ. გამანაწილებელი ფარი 3DB-2	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
27 ელ. გამანაწილებელი ფარი 3DB-3	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
28 ელ. გამანაწილებელი ფარი 3DB-4	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
29 ელ. გამანაწილებელი ფარი 4DB-1	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
30 ელ. გამანაწილებელი ფარი 4DB-2	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
31 ელ. გამანაწილებელი ფარი 4DB-3	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
32 ელ. გამანაწილებელი ფარი 4DB-4	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
33 ელ. გამანაწილებელი ფარი 4DB-5	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
34 ელ. გამანაწილებელი ფარი 5DB-1	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
35 ელ. გამანაწილებელი ფარი 5DB-2	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		

Project: ?????
Date: Wed 5/23/18 15:13

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: ?????
Date: Wed 5/23/18 15:13


Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Task Name	Duration	Start	Finish	Predecessors	
39 ელ. გამანაწილებელი ფარი 3DB-5	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
40 ელ. გამანაწილებელი ფარი 4DB-6	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
41 ელ. გამანაწილებელი ფარი DB-1 (საქვაბე)	12 days	Mon 8/6/18 8:00	Tue 8/21/18 17:00		
42 დიზელ გენერატორი	4 days	Mon 8/20/18 8:00	Thu 8/23/18 17:00		
43 უწყვეტი კვების წყარო	4 days	Mon 8/20/18 8:00	Thu 8/23/18 17:00		
44 ვენტილაცია	61 days	Tue 5/29/18 8:00	Tue 8/21/18 17:00	2	
45 მოდინებითი სისტემები	61 days	Tue 5/29/18 8:00	Tue 8/21/18 17:00		
46 AHU-ს სისტემების მონტაჟი	10 days	Wed 8/1/18 8:00	Tue 8/14/18 17:00		
47 ჰაერსატარების გაყვანა	50 days	Tue 5/29/18 8:00	Mon 8/6/18 17:00		
48 ცხაურები	15 days	Wed 8/1/18 8:00	Tue 8/21/18 17:00		
49 გამწოვი სისტემები	61 days	Tue 5/29/18 8:00	Tue 8/21/18 17:00		
50 ვენტილატორების მონტაჟი	10 days	Wed 8/1/18 8:00	Tue 8/14/18 17:00		
51 ჰაერსატარების გაყვანა	34 days	Tue 5/29/18 8:00	Fri 7/13/18 17:00		
52 ცხაურები	15 days	Wed 8/1/18 8:00	Tue 8/21/18 17:00		
53 მილგაყვანილობა	10 days	Tue 5/29/18 8:00	Mon 6/11/18 17:00		
54 გათბობა/გაგრილება	56 days	Tue 5/29/18 8:00	Tue 8/14/18 17:00	2	
55 ჩილერების მონტაჟი	10 days	Wed 8/1/18 8:00	Tue 8/14/18 17:00		
56 ქვების და ბოილერის მონტაჟი	10 days	Wed 8/1/18 8:00	Tue 8/14/18 17:00		
57 ფანკოილების მონტაჟი	39 days	Tue 5/29/18 8:00	Fri 7/20/18 17:00		
58 ფანკოილის სისტემის მილგაყვანილობა	45 days	Tue 5/29/18 8:00	Mon 7/30/18 17:00		
59 მულტი სპლიტი	7 days	Mon 8/6/18 8:00	Tue 8/14/18 17:00		
60 სპლიტი კასეტური	7 days	Mon 8/6/18 8:00	Tue 8/14/18 17:00		
61 კანალიზაცია	55 days	Tue 5/29/18 8:00	Mon 8/13/18 17:00	2	
62 წყალსადენის მოწყობა	25 days	Tue 5/29/18 8:00	Mon 7/2/18 17:00		
63 წყალსადენის გარე ქსელის მოწყობა	20 days	Tue 7/17/18 8:00	Mon 8/13/18 17:00		
64 კანალიზაციის მოწყობა	25 days	Tue 5/29/18 8:00	Mon 7/2/18 17:00		
65 კანალიზაციის გარე ქსელის მოწყობა	20 days	Tue 7/17/18 8:00	Mon 8/13/18 17:00		
66 სახანძრო უსაფრთხოება	59 days	Tue 5/29/18 8:00	Fri 8/17/18 17:00	2	
67 მილგაყვანილობა	51 days	Tue 5/29/18 8:00	Tue 8/7/18 17:00		
68 ტუმბოების მონტაჟი	6 days	Fri 8/10/18 8:00	Fri 8/17/18 17:00		
69 სუსტი დენები	33 days	Tue 5/29/18 8:00	Thu 7/12/18 17:00	2	
70 კომპიუტერული ქსელები	33 days	Tue 5/29/18 8:00	Thu 7/12/18 17:00		
71 IP ტელეფონი	33 days	Tue 5/29/18 8:00	Thu 7/12/18 17:00		
72 დამკვების სისტემა	33 days	Tue 5/29/18 8:00	Thu 7/12/18 17:00		
73 IP ვიდეომეთვალყურეობა	33 days	Tue 5/29/18 8:00	Thu 7/12/18 17:00		

Project: ?????
Date: Wed 5/23/18 15:13

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Project: ?????
 Date: Wed 5/23/18 15:13

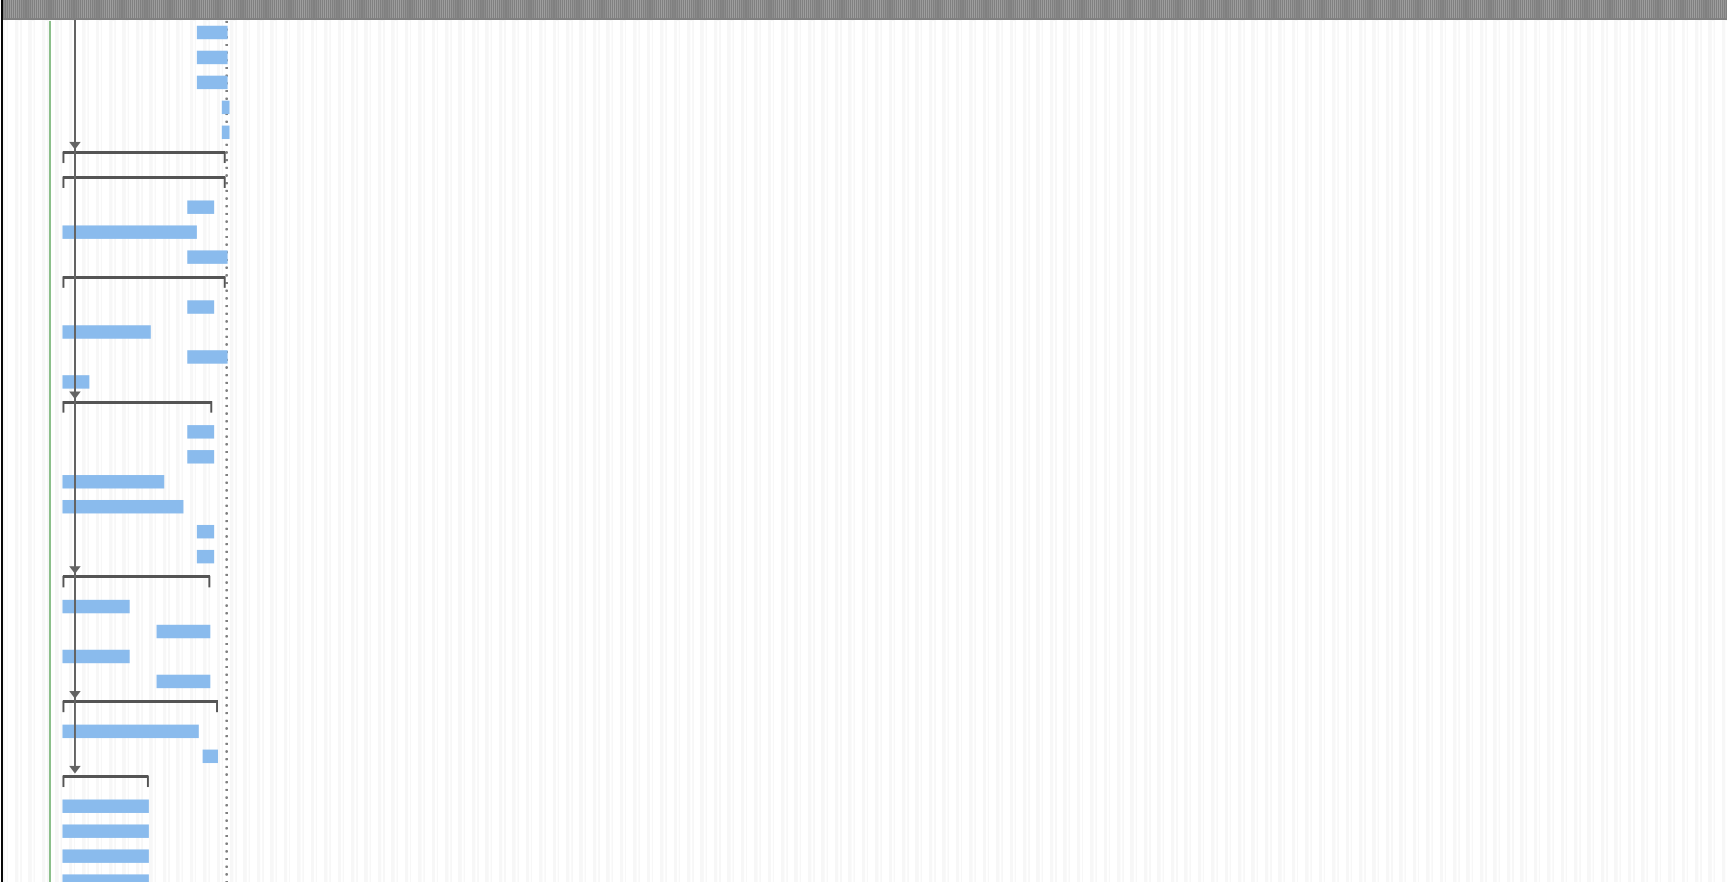

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
